



City Project No. 23-067 Bid Package 1

Fiscal Year 2025-26, Quarter 1 (7/01/25 - 9/30/25)


Funding Source		Expenses	
Federal Funds		Project Budget	\$ 3,219,411.30
State Funds	\$ -	Total Expended	\$ 2,737,991.55
Measure L Funds	\$ 3,219,411.30		
Other			
Total	\$ 3,219,411.30	Available	\$ 481,419.75

Project Details and Status:

City Project 23-067 Bid Package 1 is a part of the City of Turlock’s Roads Program and rehabilitates a total of 7,305 linear feet of roadway. Project scope consists, in general, of curb, gutter, sidewalk and alley approach reconstruction, ADA curb ramp construction, cold planing of existing roadway, pavement rehabilitation using full depth reclamation with cement (FDR-C), adjusting existing manholes and valve covers to grade, signing and striping, and traffic control.

Completion Date: October 2025

Phase: Close-Out

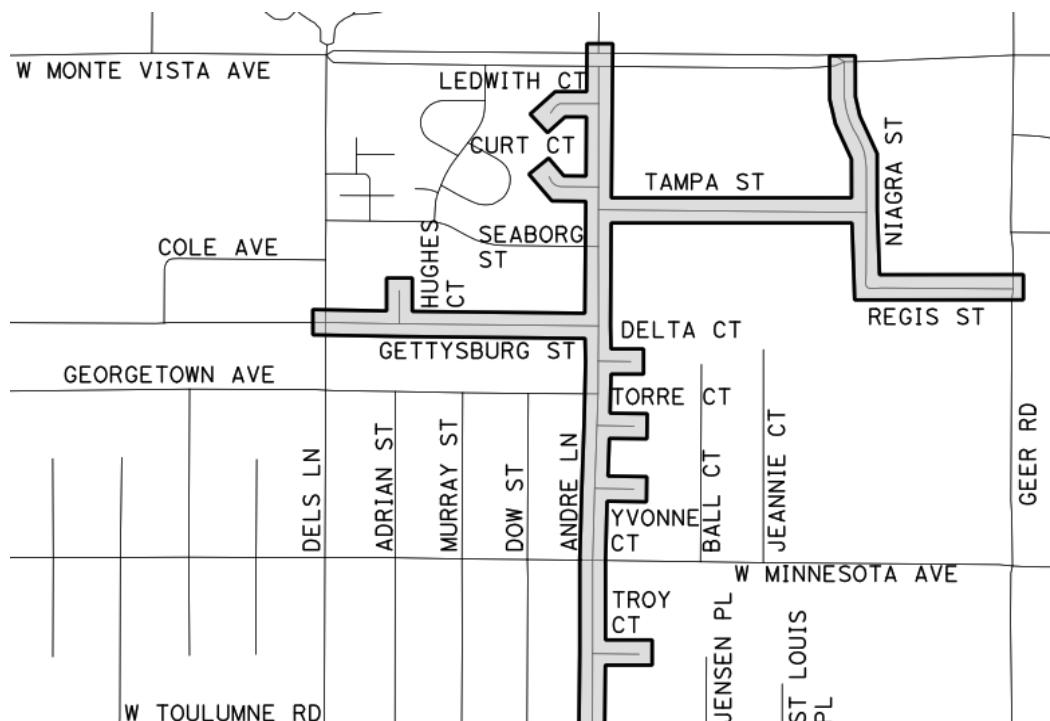



Gettybburg Drive



Andre Lane



Niagra Street



Tampa Street



City Project No. 23-067 Bid Package 2

Fiscal Year 2025-26, Quarter 1 (7/01/25 - 9/30/25)


Funding Source		Expenses	
Federal Funds		Project Budget	\$ 2,728,590.66
State Funds	\$ -	Total Expended	\$ 94,722.31
Measure L Funds	\$ 2,728,590.66		
Other			
Total	\$ 2,728,590.66	Available	\$ 2,633,868.35

Project Details and Status:

City Project 23-067 Bid Package 2 is a part of the City of Turlock's Roads Program and rehabilitates a total of 5,492 linear feet of roadway. Project scope consists, in general, of curb, gutter, sidewalk and alley approach reconstruction, ADA curb ramp construction, cold planing of existing roadway, pavement rehabilitation using full depth reclamation with cement (FDR-C), adjusting existing manholes and valve covers to grade, signing and striping, and traffic control.

Completion Date: February 2026

Phase: Close-Out

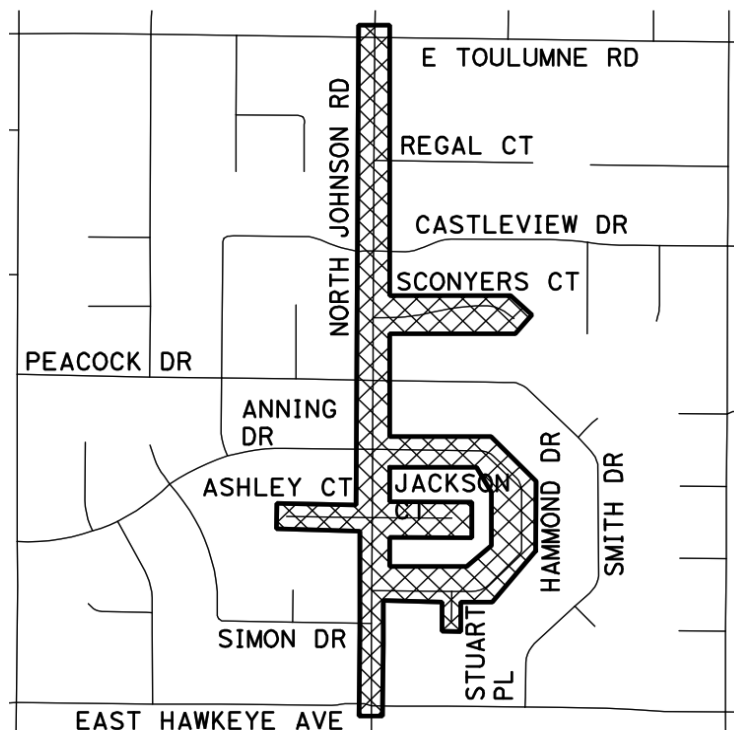



N. Johnson Road



N. Johnson Road



Hammond Drive



Sconyers Court



City Project No. 23-067 Bid Package 3

Fiscal Year 2025-26, Quarter 1 (7/01/25 - 9/30/25)


Funding Source		Expenses	
Federal Funds		Project Budget	\$ 8,025,215.00
State Funds	\$ -	Total Expended	\$ 2,921,838.18
Measure L Funds	\$ 8,025,215.00		
Other			
Total	\$ 8,025,215.00	Available	\$ 5,103,376.82

Project Details and Status:

City Project 23-067 Bid Package 3 is a part of the City of Turlock’s Roads Program and rehabilitates a total of 14,501 linear feet of roadway. Project scope consists, in general, of curb, gutter, sidewalk and alley approach reconstruction, ADA curb ramp construction, cold planing of existing roadway, pavement rehabilitation using full depth reclamation with cement (FDR-C), adjusting existing manholes and valve covers to grade, signing and striping, and traffic control.

Completion Date: May 2026

Phase: Construction

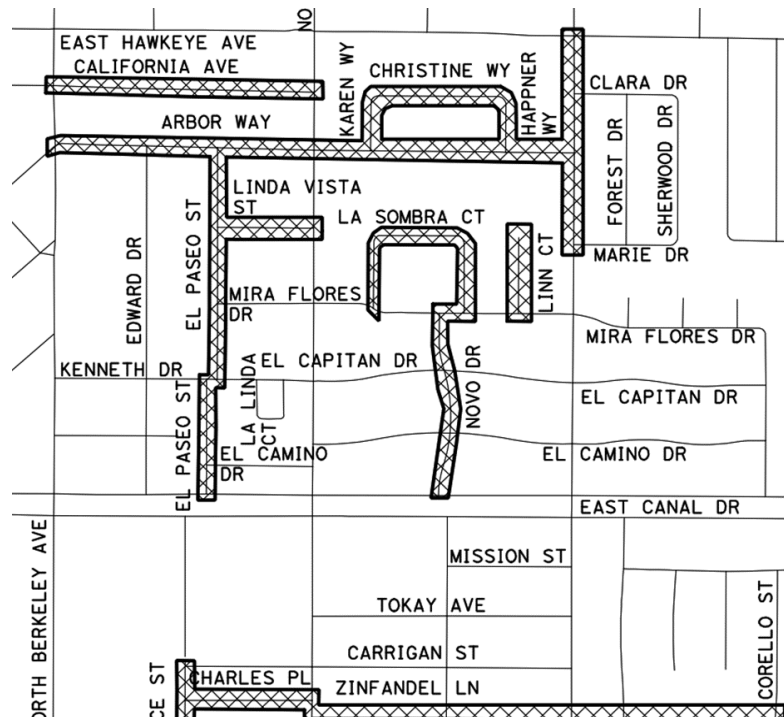



City Project No. 23-068 Bid Package 1

Fiscal Year 2025-26, Quarter 1 (7/01/25 - 9/30/25)


Funding Source		Expenses	
Federal Funds		Project Budget	\$ 1,670,859.13
State Funds	\$ -	Total Expended	\$ 1,569,513.83
Measure L Funds	\$ 1,670,859.13		
Other			
Total	\$ 1,670,859.13	Available	\$ 101,345.30

Project Details and Status:

City Project 23-068 Bid Package 1 is a part of the City of Turlock's Roads Program and rehabilitates a total of 5,058 linear feet of roadway. Project scope consists, in general, of curb, gutter, sidewalk and alley approach reconstruction, ADA curb ramp construction, cold planing of existing roadway, pavement rehabilitation using full depth reclamation with cement (FDR-C), adjusting existing manholes and valve covers to grade, signing and striping, and traffic control.


Completion Date: August 2025

Phase: Close-Out

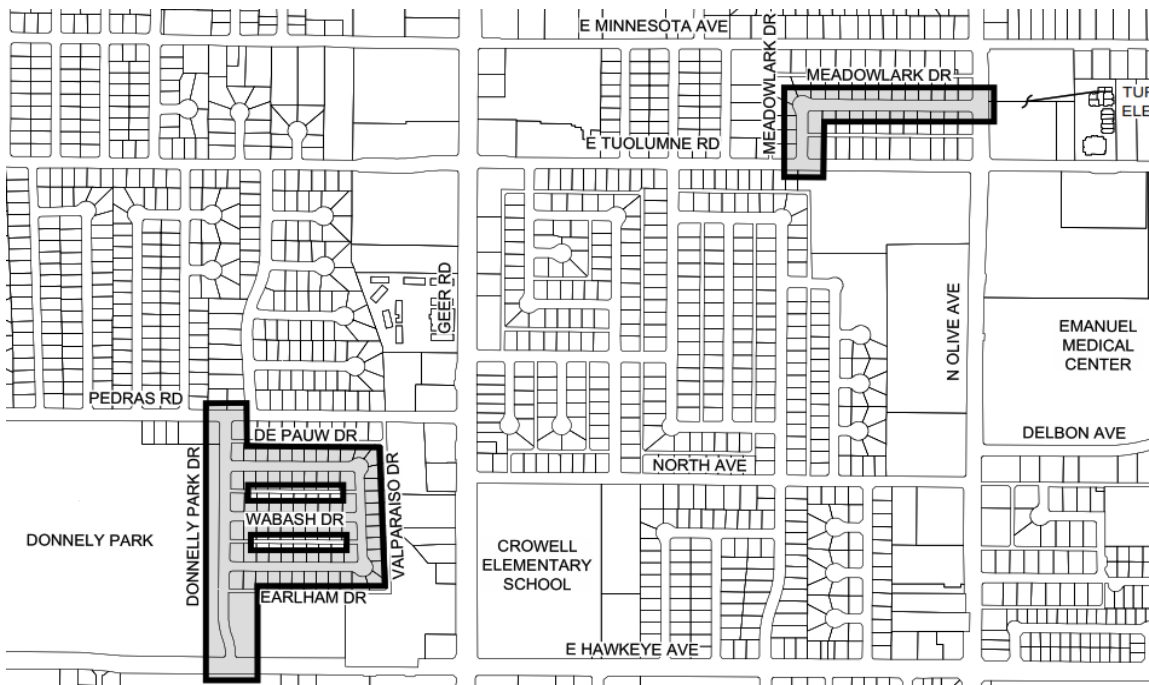



Donnelly Park Drive

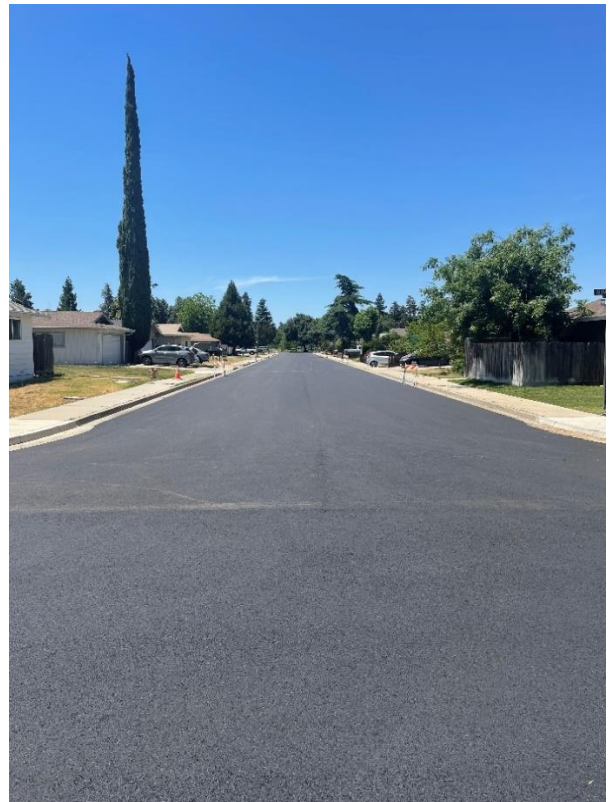

Wabash Drive



Meadowlark Drive



Meadowlark Drive



Pedras Road Rehabilitation, City Project No. 21-021

Fiscal Year 2024-2025, Quarter 1 (7/01/25 - 9/30/25)

Project Budget	\$ 1,903,356.29
-----------------------	------------------------

Funding Source		Actual Expenses	
Federal	\$ 873,883.00	Federal	\$ 869,356.29
State	\$ -	State	
Measure L	\$ 1,029,473.29	Measure L	\$ 1,034,000.00
Other	\$ -	Other	
Total	\$ 1,903,356.29	Available	\$ 1,903,356.29

Project Details and Status:

The project has rehabilitated aged pavement on Pedras Road between Geer Road and Golden State Boulevard. It includes construction of accessible pedestrian ramps, removing a valley gutter and installing storm drain improvements, and placement of new traffic striping . Notice of Completion is estimated February 2026.

Completion Date: February 2026

Phase: Post Construction

